

AITKIN COUNTY
CERTIFICATE OF INSTALLATION/~~NOTICE OF NONCOMPLIANCE~~

This certificate of installation/~~notice of noncompliance~~ has been issued this _____ day of _____, 20____ to certify compliance/~~noncompliance~~ with Aitkin County's Subsurface Sewage Treatment System Ordinance.

The premises covered by this certificate are legally described as: _____

Section _____ Township _____ Range _____ Lake _____
PERMIT NO. _____ Owner Name _____
Address _____
Installer Name _____
Type of System Inspected _____
Parcel Number _____

The certificate of installation/~~notice of noncompliance~~ was based on No ___ of the following:

- 1) Inspection of the installation or construction as in accordance with the above referenced permit and application design.

- 2) Review of as-built plans submitted in accordance with Subdivision 9.2 D of Aitkin County's Subsurface Sewage Treatment System Ordinance.

If the above permitted subsurface sewage treatment system is in noncompliance with Aitkin County's Subsurface Sewage Treatment System Ordinance, then the following shall serve as a Notice of Violation:

- 1) Statement of the findings of fact through inspections or investigations:

- 2) List of specific violations of Ordinance: _____

- 3) Requirements for correction or removal of violations: _____

- 4) Time schedule for compliance: _____

Failure to correct or remove the above violation(s) will result in this matter being turned over to the Aitkin County Attorney's Office for further legal action, which may result in revocation of licenses or registrations, fines and/or imprisonment.

INSPECTOR SIGNATURE _____

**SUBSURFACE SEWAGE TREATMENT SYSTEM INSPECTION FORM
AITKIN COUNTY, MINNESOTA**

Township Farm Island Date of Inspection 5/29/2020 I App. Number 2019-5375
10/27/2020 F App. Number 44808
 Owner Robert Folsom Parcel Number 07-0-046003
 Project Address 30020 414th Pl. Installer John Benson
 City Aitkin Zip Code 56431 T1 3BR PB

New Repair

DIST. or DROP BOX & TYPE PB

SETBACKS:

Buildings to tank(s) 75'

Buildings to drainfield 90'+

Well(s) 50' or 100' DW: 50'+ to tank

Lake/Creek/Wetland Spirit Lake: 87' to tank

TRENCHES, BEDS, OR GRAVELLESS LEACHFIELD:

Trench/Bed depth 3' to bottom

Trench/Bed length 44'

Trench/Bed bottom width 13'

Trench spacing 4 laterals

Drainfield rock below pipe 9"

Size of gravelless pipe NA

Depth of backfill 12"

Absorption area: square feet 572 ft²

lineal feet —

SEPTIC TANKS:

New Existing

Number of tanks installed 1 Tac 1650 Combo

Liquid capacity and type 1120 part combo

Type of baffle Plastic

Inspection pipes —

Manholes size 24"

Manhole to grade Yes No

PUMPS:

New Existing

Tank capacity and type 533 part combo

Pump manufacturer & model # Zoeller 152

Horsepower & GPM 0.5 HP 34 GPM

Feet of head 19'

Gallons per cycle 75 GPC

Size of discharge line 1.5"

Type & location of alarm Elec on tank

Water meter NA

MOUNDS:

Percent slope —

Upslope sand width —

Downslope sand width —

Sideslope sand width —

Drainfield rock below pipe —

Depth of sand below rock —

Perforation size & spacing 1/32" / 36" sp


Pipe size & spacing 1.5" / 3' sp

Dimensions of rock bed —

Dimensions of sand base —

Final cover —

DRAWING OF SYSTEM: (include soils)

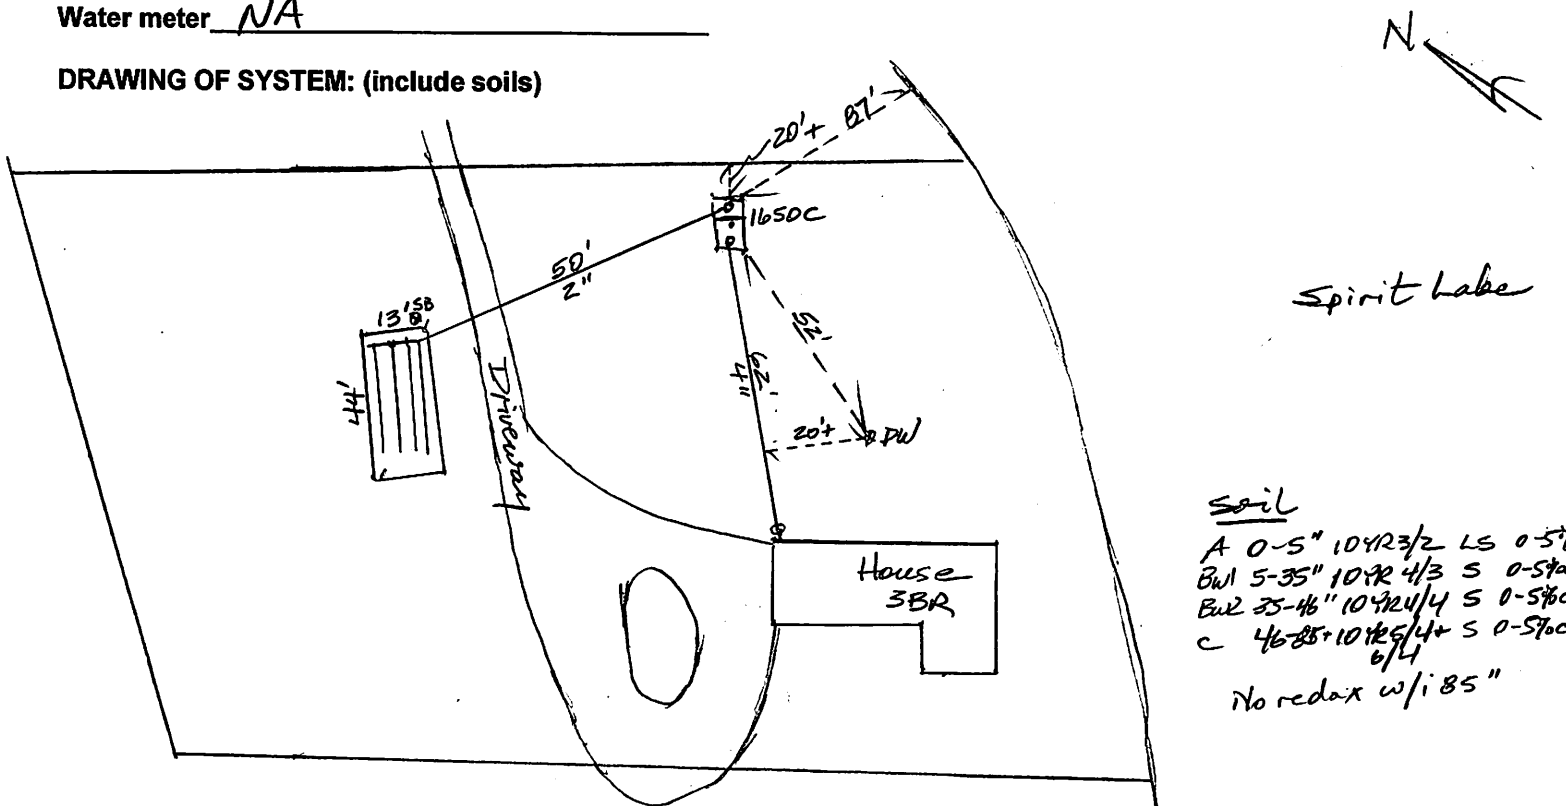

Inspector's Comments: 62' to c/p 4" 2" pipe ins under driveway 50'

Inspector's Signature Bryan Hargrave Installer's Signature _____



2020/05/29



2020/05/29



2020/05/29



2020/05/29



2020/05/29



A

B

1630

1630

2020/05/29



2020/05/29



2020/05/29
